Orig Dur	Early Start	Early Finish	
			TF Coil Repair
30	19MAY03*	27JUN03	Machine Conductors
19	18JUN03*	15JUL03	Prep Conductors
20	07JUL03*	01AUG03	Insulate Conductors
50	14JUL03*	22SEP03	Assemble/Mold TF Bundle
10	23SEP03	06OCT03	Finish/Silver Plate Contacts/Inst Shlds
4	07OCT03	10OCT03	Test TF Bundle
20	13OCT03	07NOV03	Fitup Upper Hub/Verify Lower Flag Joints
2	10NOV03	11NOV03	Re-Install TF Bundle into CS
13	12NOV03	02DEC03	Inst Lwr Clam Shell/Inst Lwr Hub & Flags
20	03DEC03	08JAN04	TF Flex/OH/CHI Bus & Clg Lines
5	09JAN04	15JAN04	Reinstall Umbr Lids/TF/CHI Outside Bus
3	16JAN04	20JAN04	Scrub
18	21JAN04	13FEB04	Pre-Op/ISTPs/Ready for Ops
84	03JUN03*	30SEP03	Fabricate New TF Flags
95	27MAY03*	08OCT03	Fabricate Flag Boxes
65	25JUN03*	25SEP03	Fabricate Hub Assembly

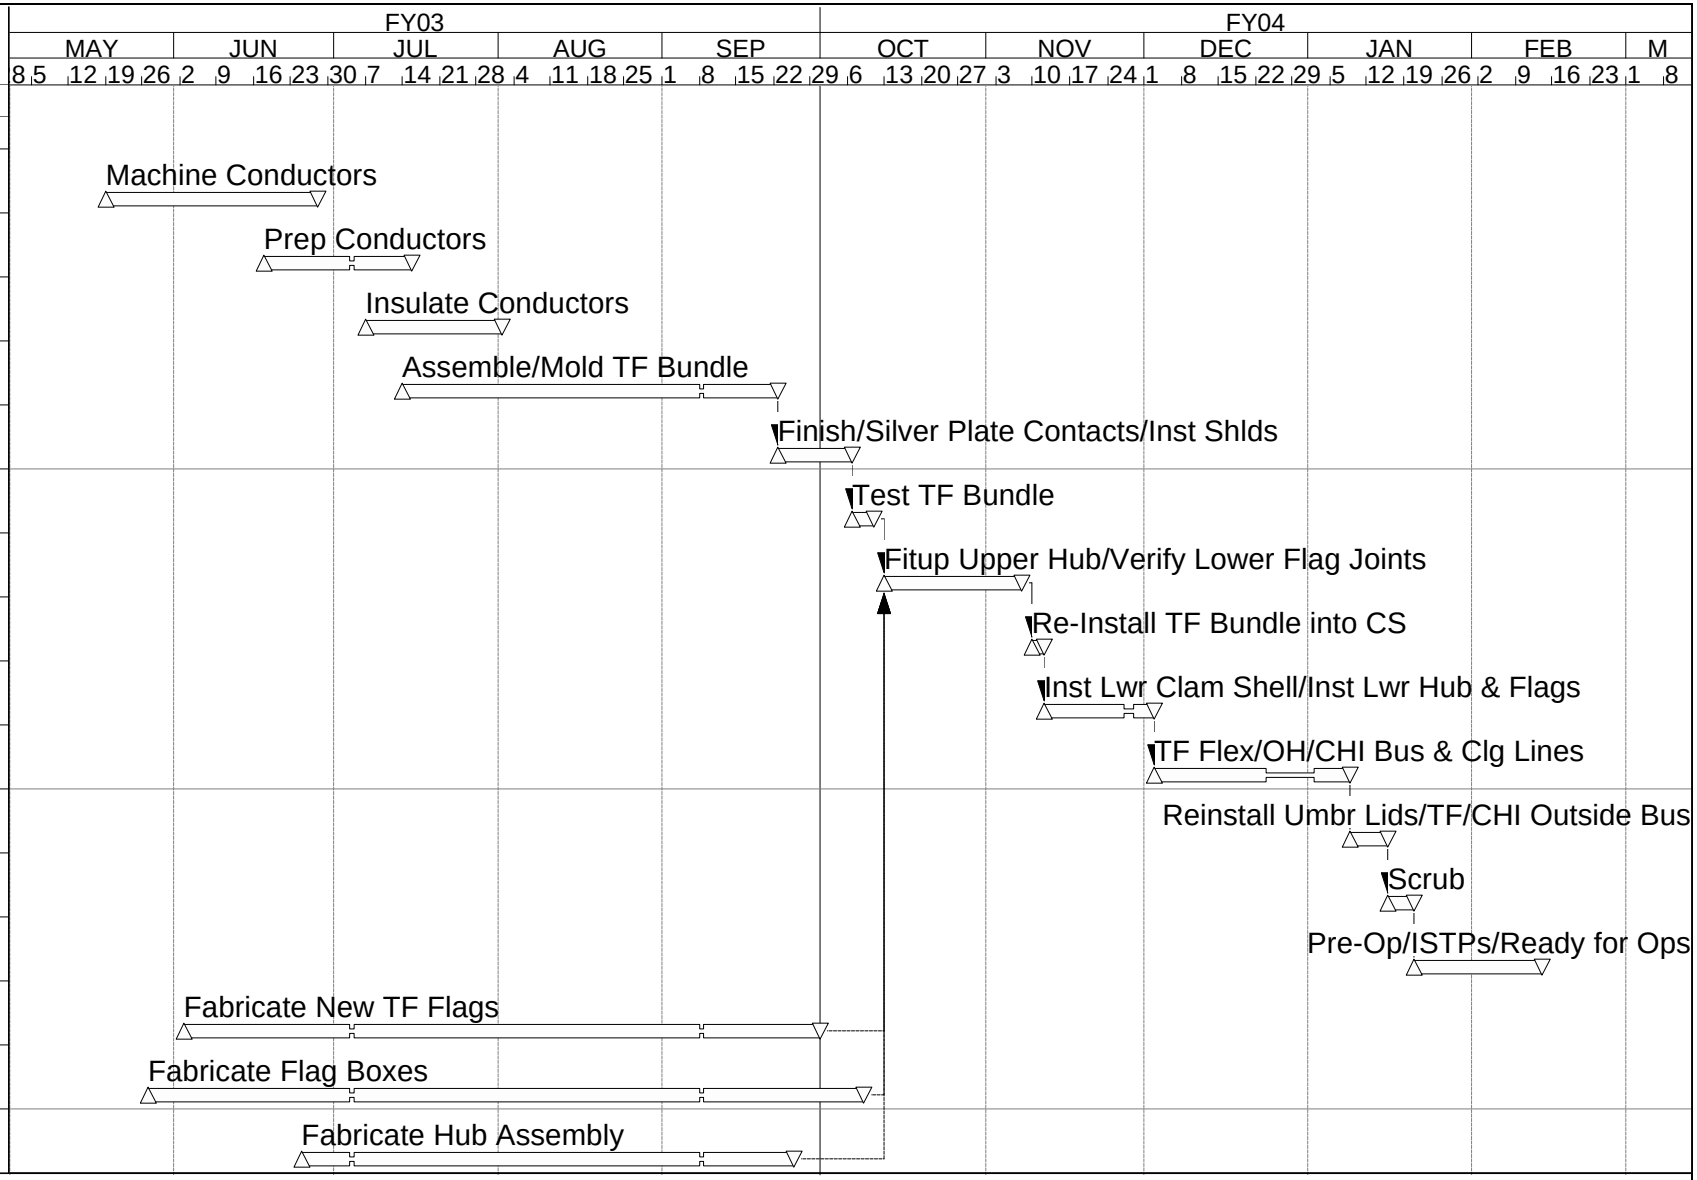

Start Date	24JUN96	NSTX TF Bundle Repair	**CBXX** **PPPL** **Sheet 1 of 1**
Finish Date	13FEB04		

© Primavera Systems, Inc.
